Chula Fondue

Project proposal and weekly progress report

Revised microservice design, architecture decisions and measured NFR evidence

Version: 1.0 | **Date:** 27 October 2026 | **Scope:** local backend progress

Executive summary

Chula Fondue provides a central place to report campus maintenance issues, route them to a responsible department and track repair progress. This revision preserves the original actors, eight use cases and product requirements [R1-R2], while documenting what the repository can actually demonstrate today.

Three NestJS services now run through Docker Compose: a REST API Gateway, a REST Department Service and a gRPC Ticket Service. They support department CRUD, ticket lifecycle/history, service-name discovery, persistent SQLite volumes, application health checks, bounded dependency calls and request correlation.

The latest local benchmark passed the provisional p95/error criteria for both ticket-list and history reads. The complete verification suite is **FAIL**, because a stopped Ticket dependency returned HTTP 504 after about 3 seconds rather than the test's expected 503. That finding remains open. Passing a local read benchmark does not establish the original 1,000-user or 99.5%-uptime requirements.

React, JWT/RBAC, Cloudinary, PostgreSQL, RabbitMQ and a MongoDB-backed Notification Service remain target work. Gmail, analytics and seven-day automatic closure remain future work. Existing notification logs are a stub, not asynchronous delivery.

Project team

Member	Student ID
Kotchapan Lertpanyaroj	6630001321
Chavapon Suwanna	6630055221
Natamathee Polerdsawat	6630092421
Piyapanchanok Meeboonsalang	6630196021
Pitchanan Thaiphayak	6632151121

This document contains the problem and use cases, service/data boundaries, three rendered architecture views, discovery/resilience decisions, NFR targets and results, remaining work, and all eleven ADRs. The companion video is a separate deliverable owned by Person 5; it is not completed by this report.

1 Problem and scope

Chulalongkorn University's buildings, faculties and public spaces experience broken air conditioners, damaged walkways, overflowing bins and failed lighting. Reports can reach unclear channels, be lost, or receive no visible follow-up. A central reporting and routing workflow makes responsibility and progress visible without requiring the reporter to know which office owns the location.

Actors and intended permissions

Actor	Intended responsibilities	Current enforcement
Reporter: student, staff or visitor	Submit issues, track own reports, cancel SUBMITTED, confirm or reopen RESOLVED	Workflow endpoints exist; identity/ownership enforcement absent
Central Admin	Review/categorize, assign/reassign or reject tickets; manage departments; view metrics	Routing/rejection/department APIs exist; category editing, admin guards and dashboards absent
Department Staff	View own queue, start work, record completion and resolve	Department filter and transitions exist; department authorization absent

Actors describe the product's requirements, not authenticated roles in today's prototype. Email and department fields supplied by callers are data, not proof of identity.

Progress boundary

Label	Meaning in this report	Examples
Implemented	Runnable code exists; verification result stated separately	Three services, SQLite, DNS, deadlines, request IDs
Proposed	Target design or integration not yet delivered	React, Auth/JWT/RBAC, Cloudinary, PostgreSQL, RabbitMQ, Notification/MongoDB
Future	Explicitly deferred beyond the next integration scope	Gmail delivery, analytics, seven-day auto-closure

Decision status is separate: original ADR-001 to ADR-008 remain Accepted as recorded in the source proposal. New ADR-009 to ADR-011 are Proposed pending team ratification, even though their local mechanisms already exist.

Functional requirements retained

The product requires registered and restricted guest access; a primarily Thai responsive mobile-browser portal without native app installation; category, building/faculty location and description; up to five photos of at most 5 MB each; admin categorization and manual routing/re-routing; department CRUD; seven ticket statuses and their history; department queues; asynchronous notification records; reporter confirmation/reopening; and later analytics/auto-closure. Current API support covers only part of that end-to-end experience. No UI, upload or authentication completion is claimed.

2 Use cases for reporting and repair

UC-01 Report campus issue

Actor: Reporter. **Trigger:** a campus maintenance issue. **Target precondition:** registered or restricted guest session. The reporter enters category, location and description, and supplies a contact email for guest access. Gateway validates up to five images, each at most 5 MB, uploads them to Cloudinary, then Ticket Service stores the report and image URLs. **Postcondition:** a new SUBMITTED ticket awaits review. Invalid required fields or media are rejected; cancellation while SUBMITTED changes the ticket to CANCELLED and removes it from the normal inbox.

Implemented: API creation validates required text fields, records history, and supports SUBMITTED cancellation. **Proposed:** portal, identity/guest restrictions, image count/size validation and uploads. The current model stores one photoUrl string; it does not implement the required multi-photo feature.

UC-02 Route ticket to department

Actor: Central Admin. **Target precondition:** authenticated admin and a SUBMITTED ticket; reassignment is allowed while ASSIGNED. The admin reviews details and selects a department maintained through UC-08. Ticket Service looks up that department, then atomically saves ASSIGNED and its history. **Postcondition:** the department queue can list the assigned ticket. An unknown department is rejected without changing ticket/history. Invalid or duplicate reports may be rejected with a reason. The target also publishes a TicketAssigned notification event for UC-05 after a successful transition.

Implemented: assignment/reassignment APIs, REST lookup, transactional history and rejection. **Proposed:** protected dashboard and RabbitMQ publishing. A failed Department lookup before commit leaves the ticket unchanged; assignment notification is currently a local log stub.

UC-03 Resolve ticket

Actor: Department Staff. **Target precondition:** a ticket assigned to that staff member's department. Staff changes ASSIGNED to IN_PROGRESS, performs repairs, supplies completion proof and resolves the ticket. **Postcondition:** status RESOLVED with reviewable proof; target status events feed UC-05.

Implemented: ASSIGNED to IN_PROGRESS to RESOLVED, with transaction/history. The current resolve RPC accepts a completionPhotoUrl and stores it in a history note. **Proposed:** staff permissions, photo upload, structured multi-photo completion storage and notification events. The API requires starting progress before resolving.

UC-04 View ticket status and history

Actor: Reporter. **Precondition:** ticket exists; target access must respect ownership. The reporter lists reports, filters them and opens a status timeline. **Postcondition:** current state and ordered history are available; unknown IDs return 404.

Implemented: list/history APIs and status, departmentId, reporterEmail and includeCancelled filters. **Proposed:** My Tickets UI, ownership enforcement and media display. The current reporterEmail filter is not an access-control mechanism.

3 Supporting and future use cases

UC-05 Record ticket notification

Actor: system-triggered; RabbitMQ is supporting infrastructure. **Precondition:** a qualifying committed ticket transition and intended recipient. Assignment, start/reopen, resolve, reject and confirmation/closure can produce the corresponding notification event. This reconciles UC-02/03/06 and the original operation catalog.

Target flow: Ticket Service publishes an event with a stable eventId to RabbitMQ. Notification Service consumes it, creates a notification record in MongoDB, then acknowledges the message. Duplicate eventId values must not create duplicate records. **Postcondition:** the record is stored and the message acknowledged. Relationships are Ticket Service, RabbitMQ and Notification/MongoDB; Gmail is not required for this use case.

If a consumer fails before acknowledgement, delivery may be repeated. If publication fails after the SQL commit, the ticket remains committed and the error is logged. This initial target can lose notifications; a durable outbox/recovery mechanism is future work before a guaranteed-delivery claim. **Current implementation:** a log stub only; RabbitMQ, consumer, MongoDB persistence and deduplication are Proposed. **Future:** Gmail email delivery. The original Gmail relationship/postcondition is superseded by this record-based flow.

UC-06 Confirm or reopen resolution

Actor: Reporter. **Precondition:** a RESOLVED ticket, with target ownership checks. The reporter reviews the repair and confirms it to change RESOLVED to CLOSED, or provides a mandatory reason to return it to IN_PROGRESS. **Postcondition:** confirmed closure or renewed work is recorded in history; target notifications use UC-05.

Implemented: confirm/reopen transitions and required reopen reason. **Proposed:** ownership UI/guards and event publication. **Future:** automatic CLOSED transition after seven days without reporter action. No scheduler currently implements it.

UC-07 Generate analytics report

Actor: Central Admin. **Target precondition:** authenticated admin and ticket data. Select dates, department/faculty and category; aggregate resolution times and recurring issue locations. **Postcondition:** MTTR and hotspot views are displayed, or an empty-state message when no data matches. **Status:** Future; there is no Analytics Service or analytics endpoint. Any later analytics design must read owned APIs/events or an explicit read model, not directly query another service's private database.

UC-08 Manage departments

Actor: Central Admin. **Target precondition:** authenticated admin. Create, list, view, update and delete departments, including name, contact email and buildings covered. **Postcondition:** updated department data is available to UC-02. Duplicate names are rejected.

Implemented: REST CRUD, DTO validation, unique names and owned SQLite persistence. **Proposed:** admin UI/guards. Department deletion and reassignment policy need further product rules; existing tickets retain the department snapshot stored at assignment.

4 Implemented service catalog

Each service is a separate NestJS application. Gateway owns transport/routing concerns; Ticket owns workflow decisions; Department owns the department directory. Runtime configuration and SQLite files are independent.

Boundary and operations	Protocol	Owned data and dependencies
API Gateway: REST ticket routes and department forwarding; /health and /ready; error translation and request correlation	HTTP REST :3000; outbound gRPC :50051 and REST :3001	No business database. Depends on Ticket and Department; serves independent routes during partial failure
Ticket Service: CreateTicket, ListTickets, GetTicketHistory, AssignTicket, CancelTicket, RejectTicket, StartProgress, ResolveTicket, ConfirmResolution, ReopenTicket and CheckHealth	gRPC :50051; outbound Department REST lookup on assign	Own Ticket and TicketHistory in /data/ticket.sqlite. NotificationStub is an internal logger, not a service
Department Service: create/list/get/update/delete departments; /health and /ready	HTTP REST :3001	Own Department in /data/department.sqlite: ID, unique name, contactEmail, buildings and timestamps

REST and RPC correspondence

Gateway routes	Ticket RPC
POST /tickets; GET /tickets	CreateTicket; ListTickets
GET /tickets/:id/history	GetTicketHistory
POST /tickets/:id/assign; DELETE /tickets/:id	AssignTicket; CancelTicket
POST /tickets/:id/reject; /start; /resolve	RejectTicket; StartProgress; ResolveTicket
POST /tickets/:id/confirm; /reopen	ConfirmResolution; ReopenTicket

Department REST uses /departments and /departments/:id through Gateway forwarding. Ticket's CheckHealth is an application-specific unary RPC, not the standard grpc.health.v1 protocol.

Ticket state and integrity

SUBMITTED permits ASSIGNED, REJECTED or CANCELLED. ASSIGNED permits reassignment or IN_PROGRESS. IN_PROGRESS permits RESOLVED; RESOLVED permits CLOSED or IN_PROGRESS with a reopen reason. CLOSED, REJECTED and CANCELLED have no further workflow transition in this prototype. Normal lists exclude CANCELLED unless includeCancelled=true. Ticket and history are saved in the same local transaction. A pre-commit dependency failure must not create a partial assignment.

5 Proposed services and data evolution

Boundary	Operations and protocol	Owned data and collaborators
Auth Service - Proposed	Register, Login, GuestLogin and token validation; REST from Gateway	Own PostgreSQL identity/role/guest data. No application or schema exists yet
Notification Service - Proposed	HandleTicketStatusChanged from RabbitMQ via AMQP; acknowledge after storage	Own MongoDB notification records with unique eventId. No Gateway-to-Notification RPC
React portal - Proposed	Report, review, route, resolve and confirm screens; Gateway REST/HTTPS	UI state only; no direct backend database access
Cloudinary integration - Proposed	Gateway validates/uploads images using HTTPS	Media content external; Ticket stores permitted URL metadata
Analytics - Future	Authorized aggregate reports/read model; contract not finalized	Own read model if introduced; no direct cross-service table access
Gmail delivery - Future	Notification delivery adapter via HTTPS	Provider credentials/consent and delivery policy not specified or implemented

Storage ownership and migration

ADR-007 retains PostgreSQL on Render as the original target for Auth, Ticket and Department, and MongoDB for Notification. Each boundary owns its database/schema and credentials. The current two SQLite databases are a prototype deviation documented openly; no cloud database is provisioned by this progress report.

Ticket owns report fields, status, assignment snapshots and history. Department owns contact/building coverage. Cross-service consistency is achieved by validating a department through its API before assignment, not by a cross-database foreign key or shared transaction. A later department edit does not automatically rewrite existing ticket snapshots.

A proposed migration must define explicit PostgreSQL schemas/migrations, export/import SQLite fixtures, reconcile ticket/history counts and IDs, run lifecycle and failure tests in staging, validate backup/restore, and retain a rollback path. Production schema management must replace automatic synchronization. Persistence across recreation proves the selected volume-backed records survive container replacement; it does not prove recovery from disk loss.

Proposed event contract

Use eventId, eventType, ticketId, recipient, occurredAt and schemaVersion as the initial event envelope to finalize. Candidate events are TicketAssigned, TicketProgressStarted, TicketResolved, TicketRejected, TicketReopened and TicketClosed. These are target contracts, not existing message implementations. SQL commit and AMQP publication are separate; record this delivery gap until a reliable publishing design is delivered.

6 Revised logical architecture

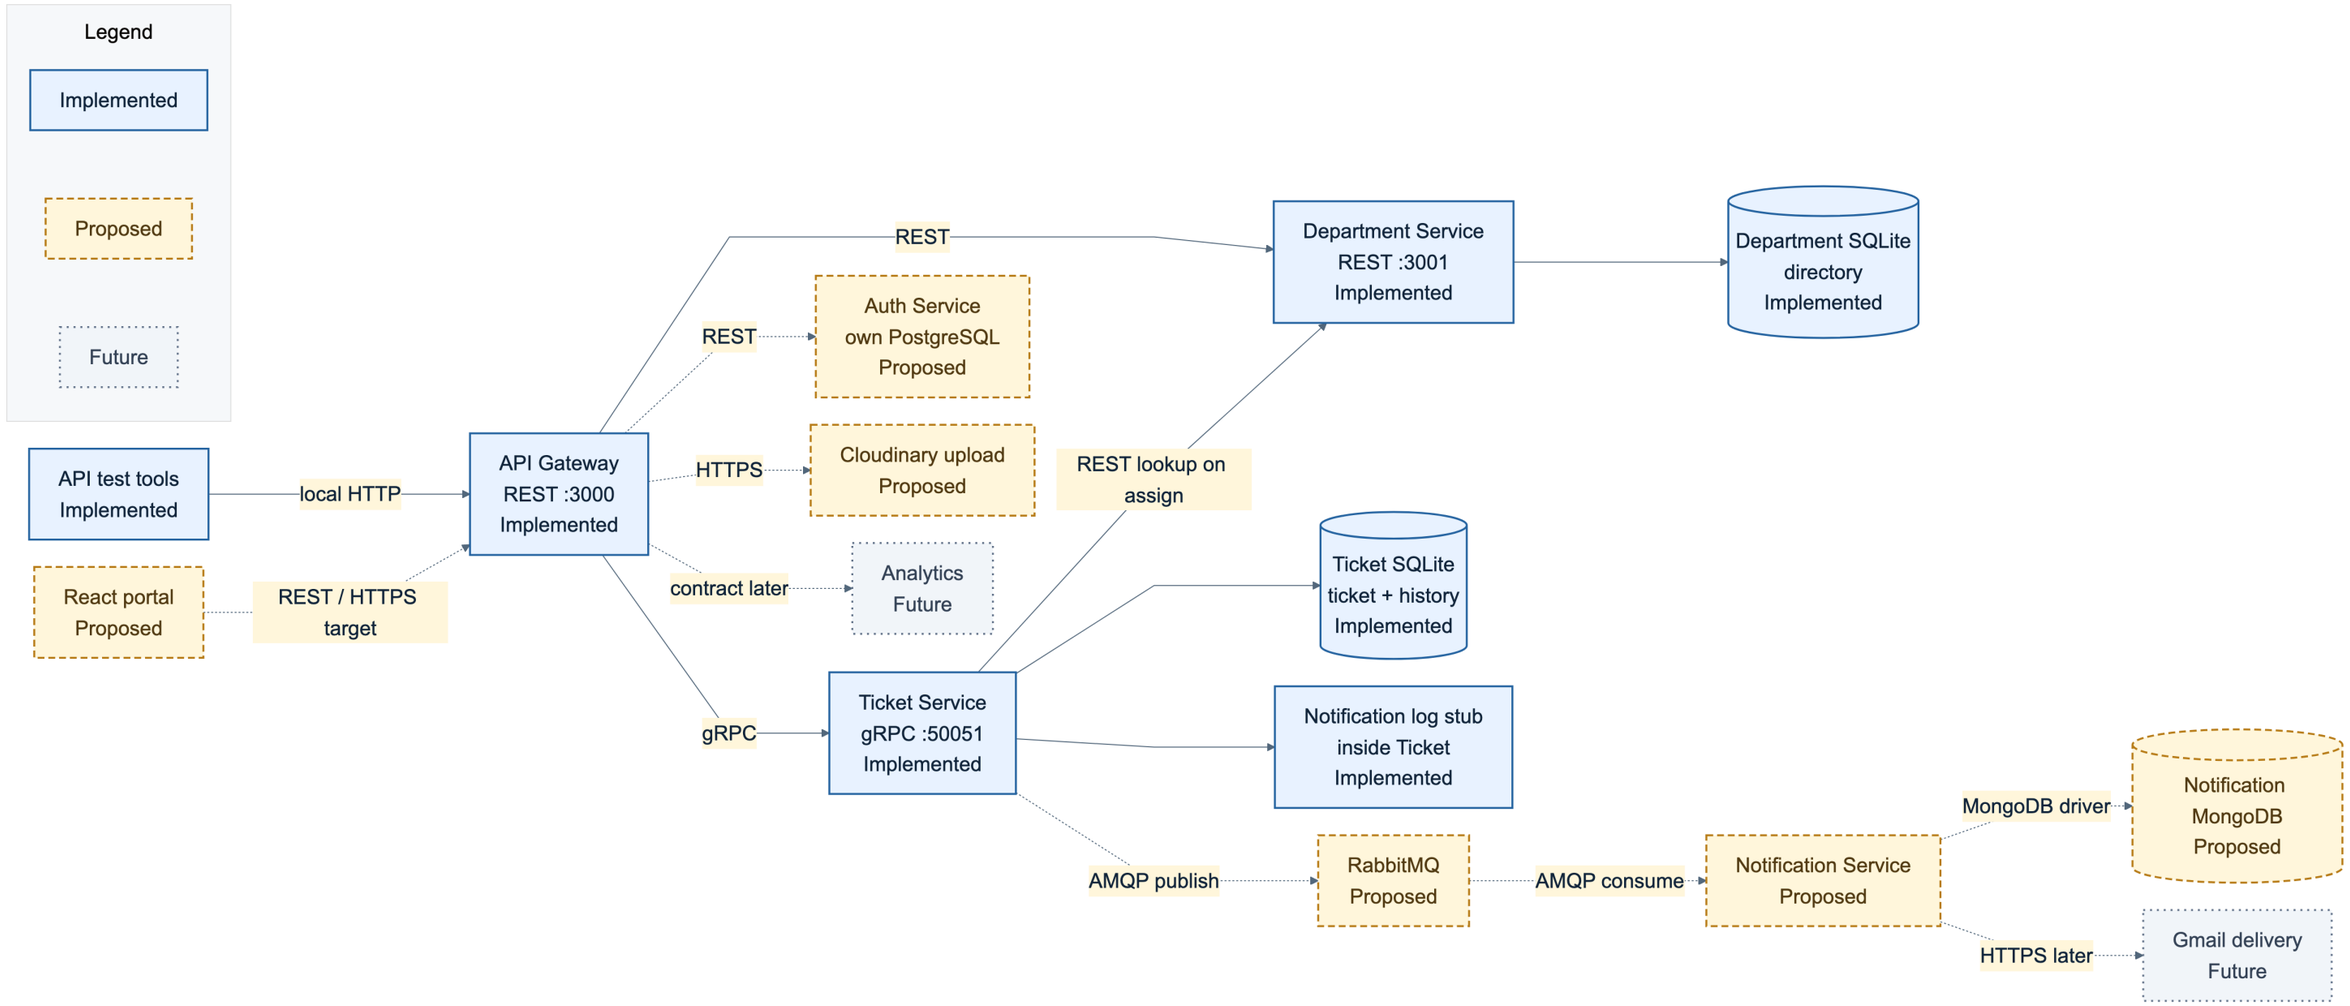


Figure 1. Implemented components are blue with solid call paths. Proposed components are amber with dashed call paths; Future components are grey. Status is written in labels as well as encoded by color. SQLite is current; PostgreSQL remains the service-owned relational target. Current local traffic is HTTP/insecure gRPC; HTTPS is a proposed deployment boundary.

7 Local deployment and discovery

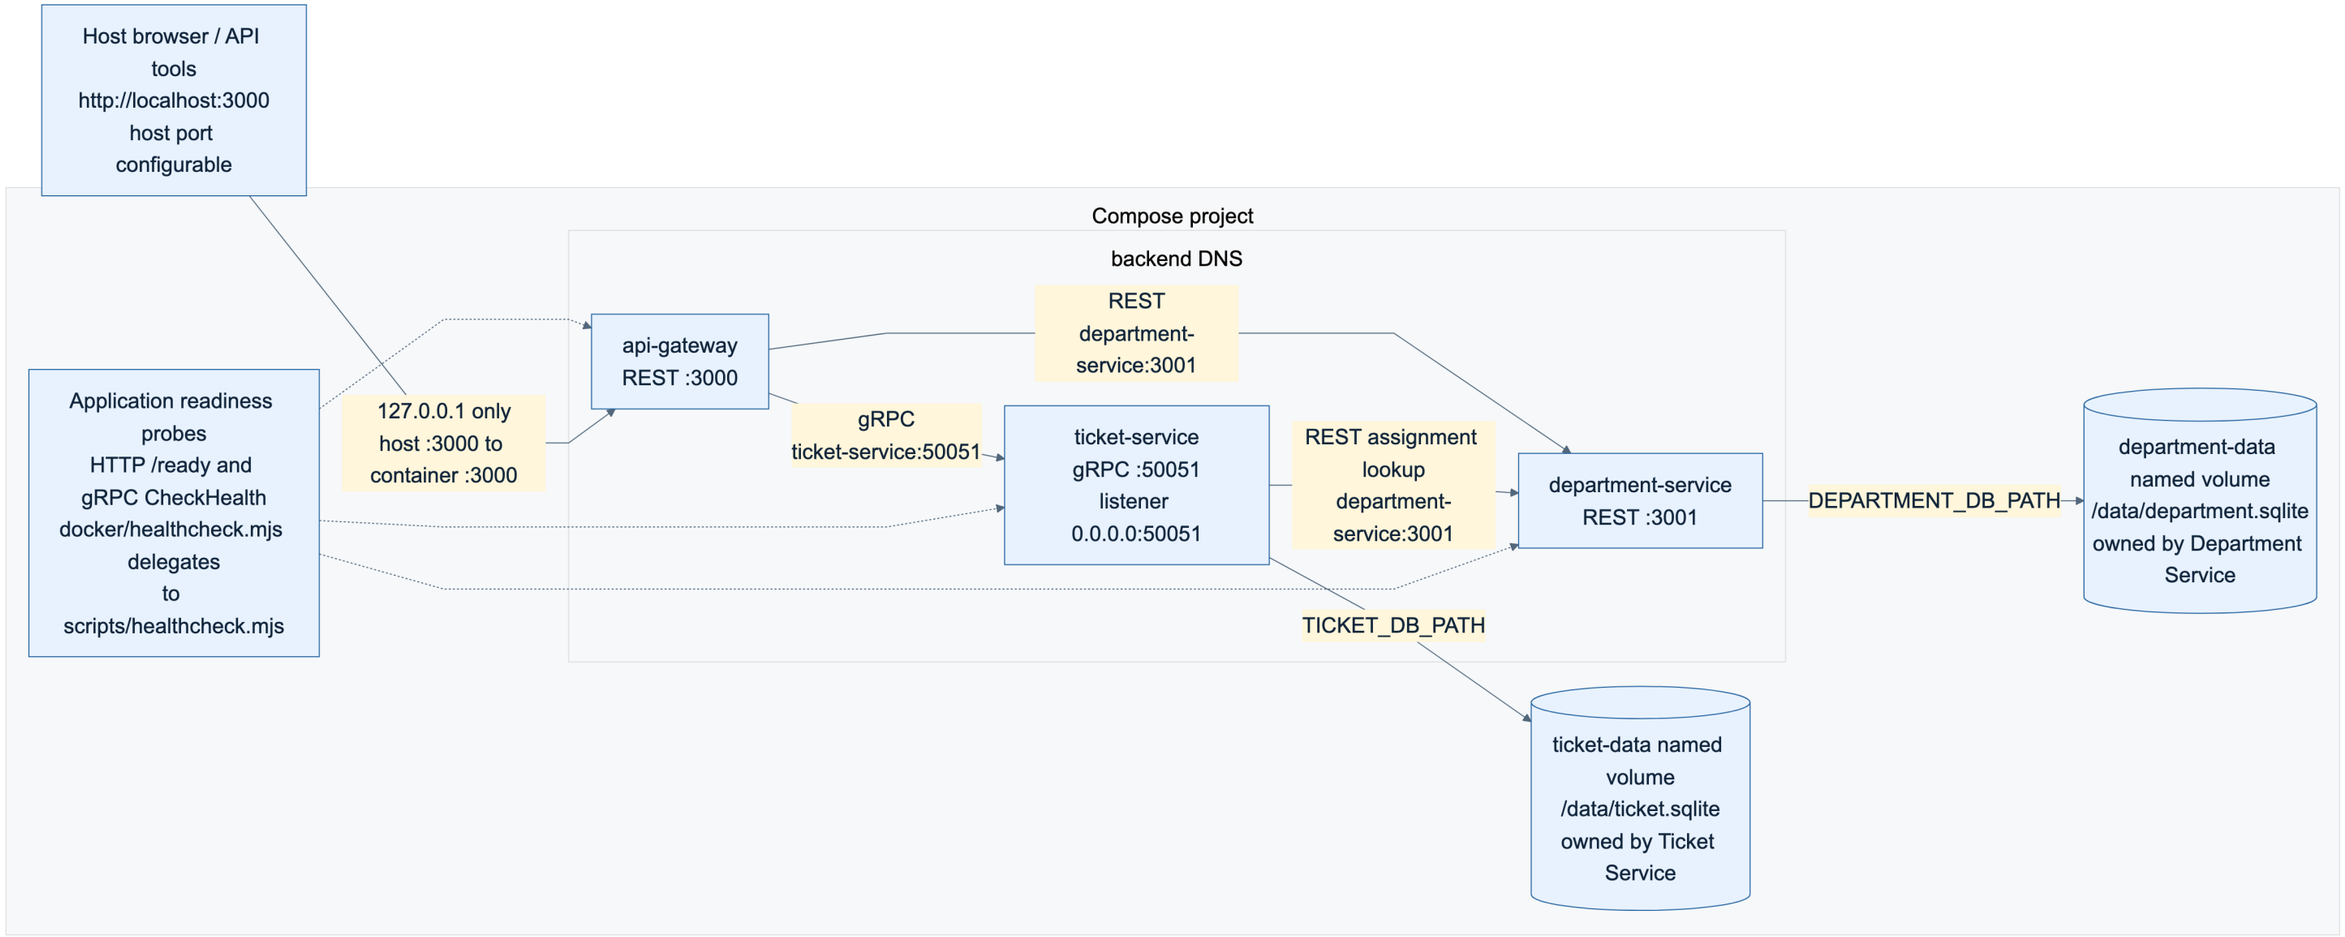


Figure 2. The host calls Gateway's published loopback port; containers use service-name DNS within the backend bridge network. Only Gateway is published. The two SQLite databases use separate named volumes. Current images include the shared application probe; older images may still use the bootstrap fallback and must be rebuilt for current behavior. This is a single-host local view.

8 Assignment sequence and failure boundary

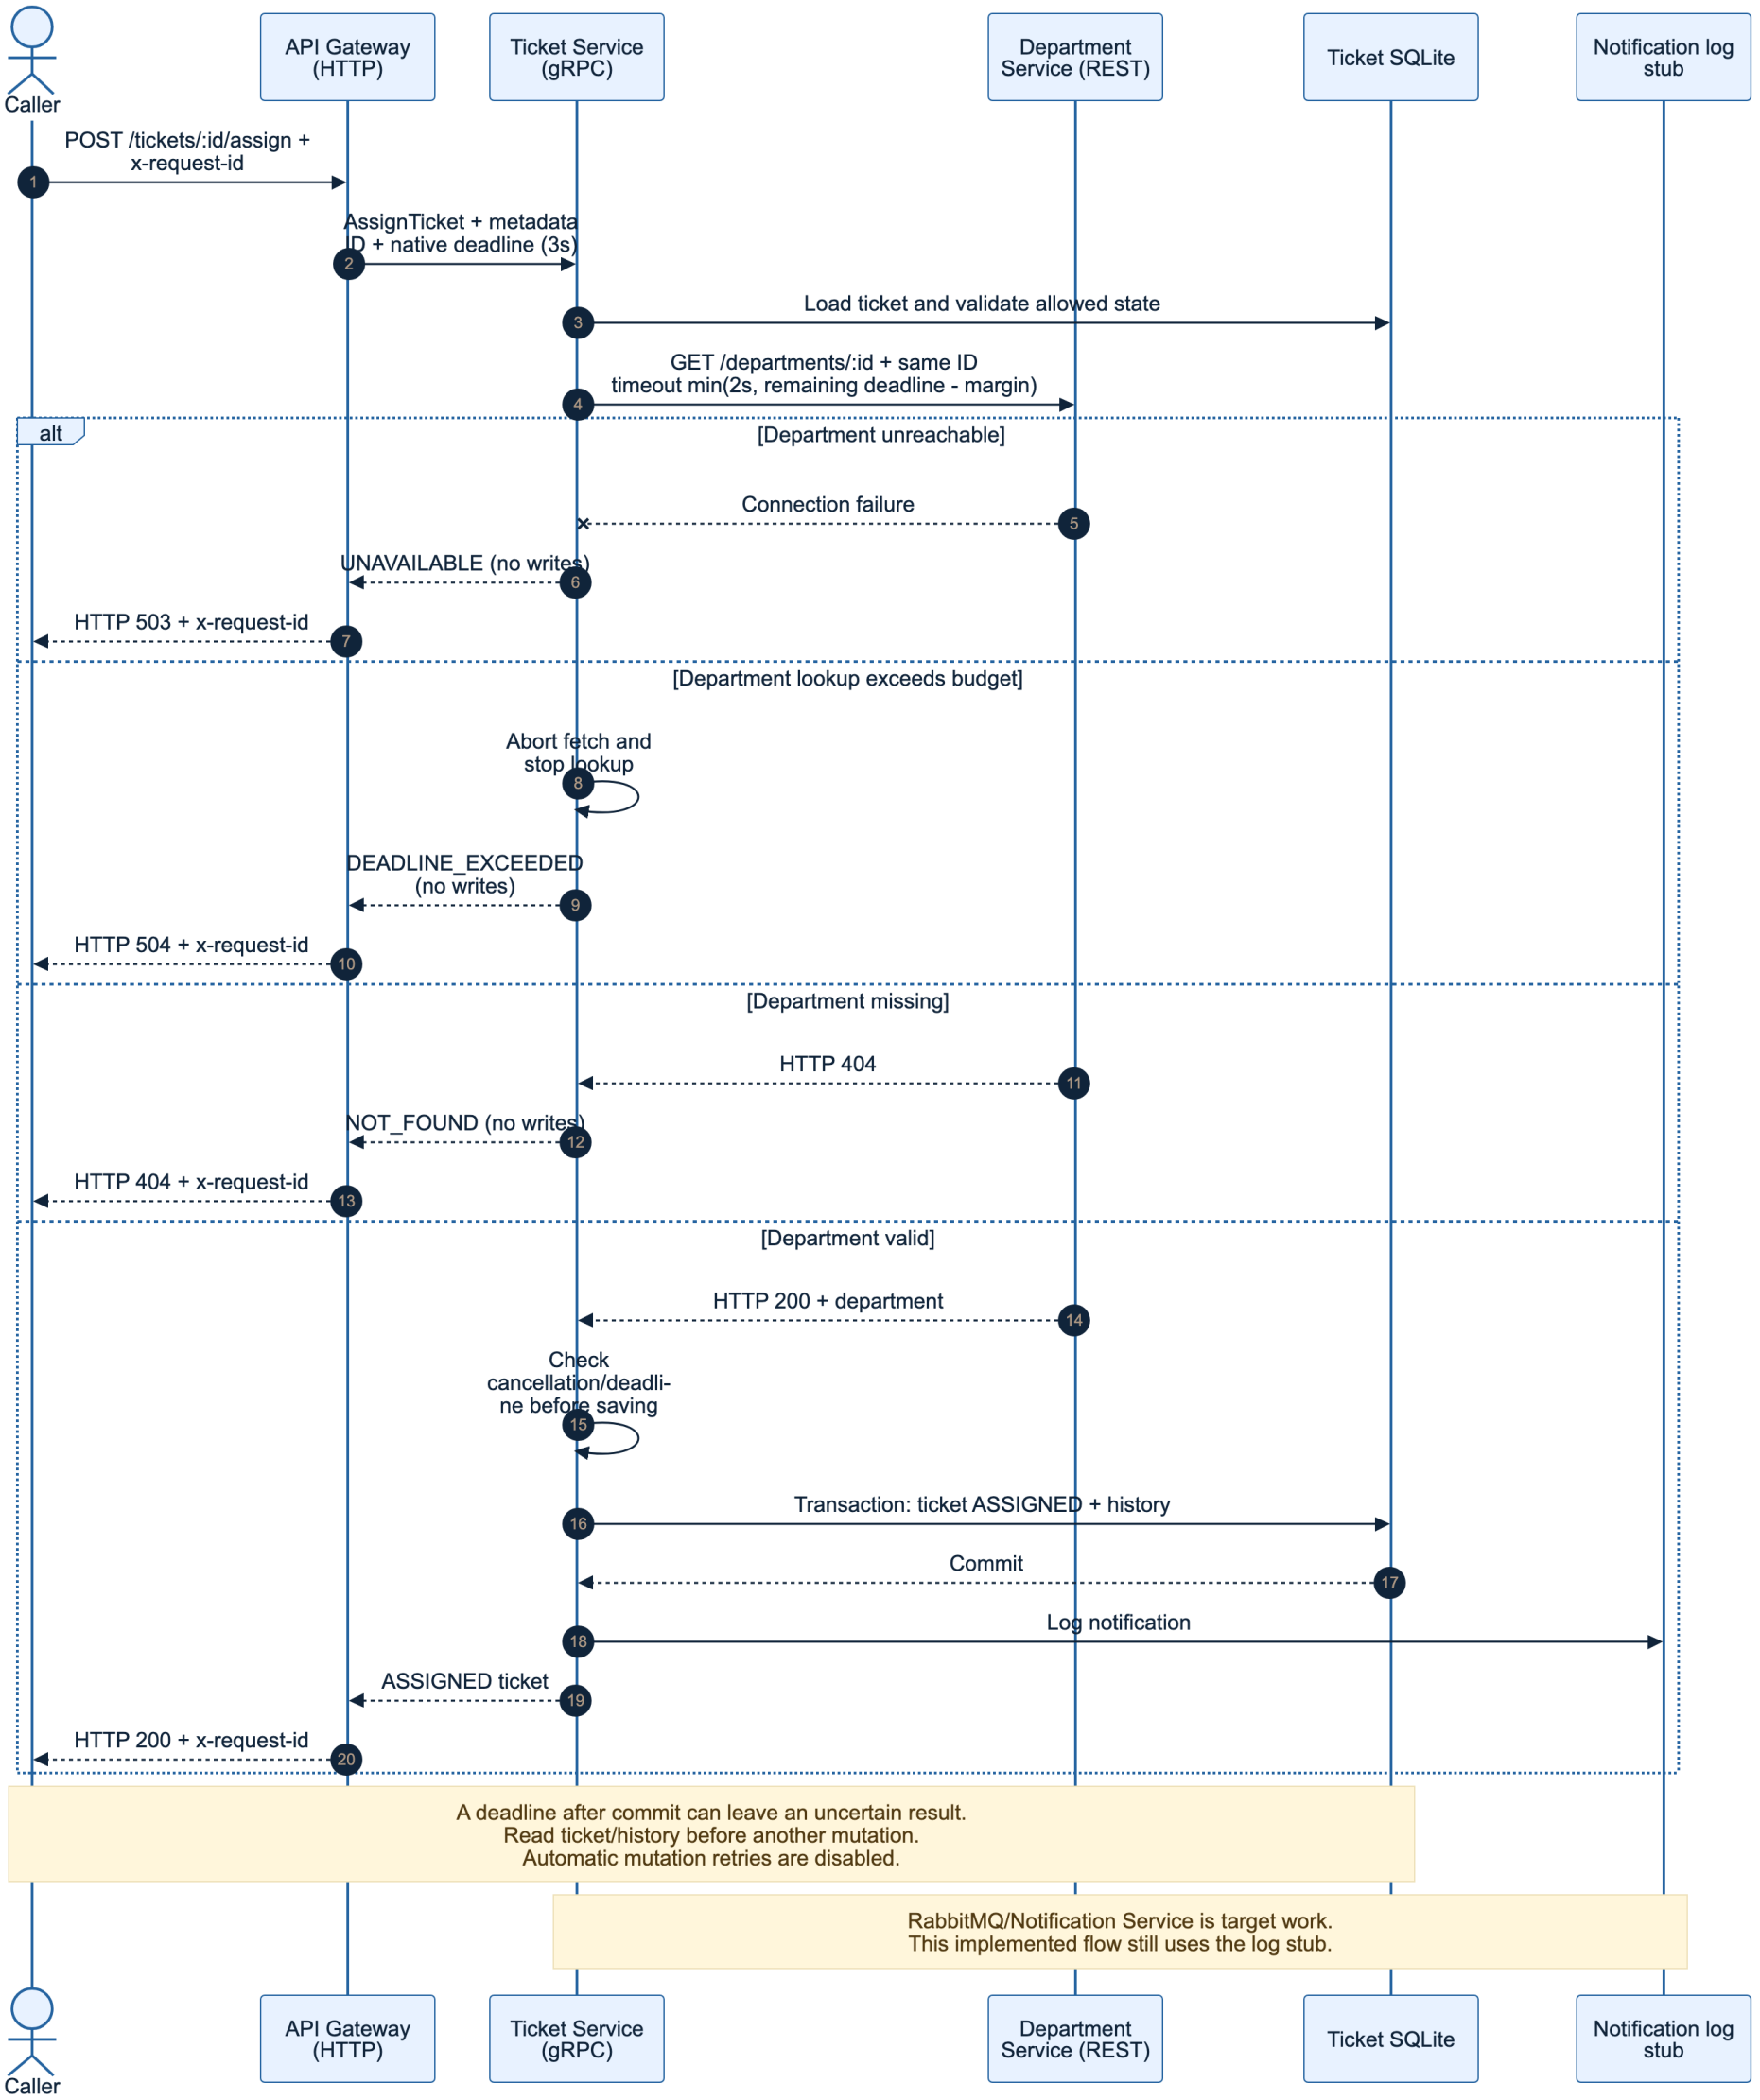


Figure 3. Implemented Gateway → Ticket → Department flow, including pre-commit failure paths and a local ticket/history transaction. The notification action shown is the current log stub. RabbitMQ publishing/consumption belongs to the proposed flow in Figure 1 and UC-05. A deadline after commit can leave an uncertain caller result; read state before retrying a mutation.

9 Discovery and resilience management

Configuration selects logical names and ports. Compose DNS resolves those names within the network; application clients must handle broken connections after replacement. Static IPs are not used. The host cannot use Compose-only names; container localhost addresses the caller itself [R3]. Actual lookup/configuration and reconnect evidence is recorded in discovery.json [E1].

Environment or caller	Destination
npm/local development	Gateway localhost:3000; Department localhost:3001; Ticket localhost:50051
Host to Compose	http://localhost:3000 by default; isolated Person 3 run used 31320
Gateway to Ticket in Compose	ticket-service:50051
Gateway/Ticket to Department in Compose	http://department-service:3001
Ticket listener	0.0.0.0:50051, not a client discovery address

Local .env values remain unchanged; Compose supplies container-specific URLs. Replacement checks preserve the original Gateway container and database volumes. Both service container IDs changed and reads succeeded without editing URLs. The run does not claim IP addresses changed; Docker can reuse them.

Health and budgets

Mechanism	Current behavior
Liveness	Gateway/Department GET /health answers independently of dependency readiness
Readiness	GET /ready checks dependencies/DB; Gateway returns 503 with separate Department/Ticket results when degraded
Ticket readiness	CheckHealth returns SERVING or NOT_SERVING and database status
Business calls	Gateway→Department REST 2,000ms including body; Gateway→Ticket native gRPC deadline 3,000ms
Assignment lookup	At most 2,000ms, shortened to remaining incoming RPC deadline minus a 25ms margin
Health checks	Application dependency/DB checks 750ms; shared probe transport budget 2s; Docker wrapper process limit 4s

Startup service_healthy ordering [R4] does not provide runtime failover, replace an unhealthy service automatically or prove uptime. A Gateway with readiness 503 can still serve independent routes. Deployment routing policy must account for this choice.

UNAVAILABLE maps to 503, DEADLINE_EXCEEDED to 504, invalid input to 400, missing records to 404 and invalid transitions to 409. Cancellation/deadline checks precede writes; no automatic mutation retry, idempotency key or circuit breaker is implemented [R5]. The repeated stopped-Ticket 504 finding is retained in Section 12 rather than relabelled as a pass.

10 NFR matrix for the implemented backend

Original requirements remain intact. The progress benchmark uses a provisional p95 criterion; it does not replace the original 1-second query requirement or establish a bound for every request.

Requirement	Target	Mechanism	Verification	Measured result	Limitation
Ticket status/history latency [R1]	Original: within 1s. Progress: p95 <1s, errors <1%	Gateway REST to gRPC, owned SQLite reads, bounded calls	100 tickets, 20 workers, 10s warm-up, 60s per endpoint; raw CSV audit	PASS for provisional p95/error target: list 27.68ms, history 23.37ms, 0% errors	Max 1,070.51/3,681.71ms; an all-request 1s ceiling is not achieved in this run
Bounded REST dependency wait	2s budget; test tolerance <3.2s	Abort timeout covers request/body and assignment lookup	Stop/freeze Department; HTTP timing and state snapshots	PASS: stopped proxy/assign 503; frozen proxy 2,010.14ms and assign 2,061.19ms, both 504	Frozen peer, not a calibrated network-delay experiment; scheduling adds delay
Bounded Ticket wait and meaningful status	3s deadline; tolerance <4.2s; stopped expectation 503	Native gRPC deadline and code mapping	Stop/freeze Ticket; liveness/readiness and independent route	Frozen PASS: 504 in 3,017.00ms. Stopped FAIL: 504 in 3,027.05ms vs 503	Mapping follows observed deadline; transport cause and stronger status expectation remain open
Assignment consistency	No state/history change when Department lookup fails before commit	Validation before write; one ticket/history transaction; cancellation checks	Deep compare before/during/after Department faults	PASS: SUBMITTED fixture and full history unchanged	Deadline after commit can be uncertain; no distributed transaction/idempotency guarantee
Local discovery and persistence	Stable service names; selected records survive replacement	Compose DNS, client reconnection and two named volumes	DNS lookup, both recreations, original Gateway ID and fixture comparison	PASS: new service containers; original Gateway; records/history unchanged	Single host, selected fixtures; not multi-host/HA, backup or disk-loss recovery
Request observability	Correlate one request through all participating services	Validated x-request-id in HTTP headers/gRPC metadata and structured logs	Assignment trace captured before recreation	PASS: same ID in 5 records across Gateway, Ticket and Department	Request correlation only; no metrics platform or full tracing backend

11 Product and production NFRs still to verify

These original targets are not satisfied by service configuration or backend read throughput alone. NOT_RUN means no applicable measurement was performed in this progress cycle.

Requirement [R1]	Original target	Proposed mechanism	Verification needed	Current result	Limitation
Usability and page load	Responsive, primarily Thai; public reporting interface <2s	React/TypeScript portal, mobile forms and accessible feedback	Real page-load tests and Thai user tasks on desktop/mobile	NOT_RUN; UI absent	Backend p95 is not page-load evidence
Image processing	Upload within 3s under normal load; up to 5 photos, <=5MB each	Gateway count/type/size checks and Cloudinary HTTPS	Upload workloads with specified image sizes/network; validation/failure tests	NOT_RUN; URL fields only	Current model is one photoUrl and completion URL in a note; no upload implementation
Availability	99.5% operational uptime during active terms	Monitored deployment, recovery, backups and an agreed SLI/window	Define academic-term observation window and outage accounting; sustained monitoring	NOT_RUN; no uptime percentage measured	Health probes and a short fault demo do not establish availability or HA
Security	JWT sessions, RBAC and restricted guests	Auth Service, Gateway authentication and service resource/department authorization	Positive/negative role, ownership, JWT and guest tests	NOT_RUN; no auth/guards	Reporter email and department filters do not enforce access control
Scalability	Up to 1,000 active users without degrading submission	Capacity design, service-owned PostgreSQL and evaluated scaling	Define session/arrival/think-time model; authenticated submission and mixed-load tests	NOT_RUN	20 closed-loop read workers and req/s are not active-user capacity
Operational compatibility	Desktop/mobile; major browsers on Windows, macOS, iOS and Android	Responsive UI and browser test matrix	Device/browser coverage, accessibility and error recovery	NOT_RUN; UI absent	Docker arm64/local API checks do not prove client compatibility

12 Measured verification and open finding

Latest run: **20261027t084152z-c1ab**, 27 October 2026, 08:41:52-08:45:22 UTC (15:41:52-15:45:22 Asia/Bangkok). Command: `node scripts/verification/run.mjs`. **Overall: FAIL**, with the per-check results below [E1-E3].

Performance evidence

The dataset contained exactly 100 tickets: 20 ASSIGNED with 2 history entries and 80 SUBMITTED with 1. Both read-only endpoint runs preceded functional mutations. Each used 10s warm-up, 20 asynchronous closed-loop workers and a 60s measurement window. List returned all 100 records; history rotated all 100 IDs. Warm-up is excluded; in-flight requests drain and count in the throughput denominator. Client latency includes full body, JSON parsing and payload verification. Percentiles are nearest-rank across all attempts; errors include non-200, transport/timeout and invalid payloads.

Endpoint	Requests	req/s	p50 ms	p95 ms	p99 ms	Error
GET /tickets	67,200	1,119.31	13.42	27.68	72.86	0%
GET /tickets/:id/history	69,113	1,151.57	9.42	23.37	54.97	0%

An independent CSV audit passed. Drain-inclusive times were 60.037s/60.016s. Maximum client latencies were 1,070.51ms/3,681.71ms; outlier causes have not been isolated. Closed-loop workers slow their arrival rate as responses slow, so this is not a fixed-arrival peak-load experiment.

Other checks and remaining failure

PASS: workflow through reopen/confirm to CLOSED, cancel/reject, filters/history, 400/404/409, request correlation, DNS, both service recreations, selected persisted records, Department stopped/frozen, Ticket frozen, restoration and shutdown.

OPEN FAIL: after stopping Ticket, GET /tickets returned **504 in 3,027.05ms**, expected 503. It happened in both full runs. The first run's actual Gateway log records gRPC DEADLINE_EXCEEDED (code 4), which current code maps to 504. A bounded response is achieved, but the stronger stopped-service classification is not. The transport cause remains unproven; Person 2 must assess implementation versus the intended contract. Expected status was not relaxed to obtain a pass.

All four fault phases restored their dependency, final readiness was 200 with both dependencies up, and the isolated project's containers/network were removed while its two named volumes were retained. Earlier runner failures in trace capture/ANSI parsing and stale-health cleanup were corrected and passed in this latest run; earlier FAIL evidence remains available.

Environment and provenance

Apple M3 arm64, 8 logical CPUs, 16 GiB RAM; Docker VM 8 CPUs and about 11.67 GiB; Engine 27.4.0, Compose 2.31.0-desktop.2; host Node v24.4.1/container Node v22.23.4. Other Compose projects shared resources. Git HEAD 52f2040e75afeb845b4bb3de10a40f4741aef818 was dirty; environment.json records 43 source/config hashes and image IDs. Do not equate that initial commit alone with the measured working tree.

13 Remaining work and release boundaries

Next progress actions

Priority	Work	Owner or coordination	Completion evidence
1	Diagnose stopped-Ticket 504 versus 503 expectation; preserve timeout and mutation safety	Person 2 with Person 3's reproduction	Documented resolution or explicit contract revision; rerun faults
2	Review and ratify ADR-009/010/011; agree original query-latency interpretation	Team	Recorded decision status and measurable criteria
3	Record the <5min discovery/NFR video using this proposal and actual evidence	Person 5	Playable clip, duration/voice/legibility checks
4	Implement JWT/RBAC and restricted guest/ownership rules; protect staff/admin actions	Subsequent development	Authorization tests across roles/resources
5	Implement React reporting/queue/timeline flows and Cloudinary validation/uploads	Subsequent development	UI/browser usability, page-load and upload measurements
6	Migrate service-owned relational stores; integrate RabbitMQ and Notification/MongoDB	Subsequent development	Migration/recovery, publish/consume/redelivery/deduplication evidence

Later and production work

Gmail delivery, analytics and seven-day automatic closure stay Future. Production preparation also requires a chosen hosting/network/TLS setup, secrets and token lifecycle, backup/restore, monitored uptime, a reliable publishing policy, mixed/concurrent-write load tests and an active-user workload model. Provider private addresses differ from Compose names; Render remains an original target, not a verified deployment [R7].

Risk register

Risk	Current consequence	Treatment
Unauthenticated APIs	Conceptual roles and ownership can be bypassed	Deliver authorization before user-facing exposure
Publish-after-commit gap	Proposed notifications can be lost	State limitation; design durable publishing/recovery before delivery guarantees
Single-host SQLite	No demonstrated replica write capacity or disk-loss recovery	Migration/capacity/backup evidence; do not infer HA from DNS/volumes
Deadline after commit	A timeout does not prove rollback	Reconcile state; design idempotency before mutation retries
Shared benchmark resources	Results vary and client overhead can affect tails	Preserve environment; repeat representative deployed workload

14 Architecture decision records

The full eleven records follow in the PDF. Their editable sources are in the ADR register. Original Accepted statuses describe recorded design intent, not feature completion; new Proposed statuses avoid assuming team approval.

ADR	Topic	Recorded decision	Implementation
001	Frontend	Accepted in source	Proposed
002	Backend	Accepted in source	Implemented subset
003	Manual routing	Accepted in source	Assignment API implemented
004	Async notification	Accepted in source	Proposed; stub today
005	Communication	Accepted in source	REST/gRPC subset implemented
006	RabbitMQ	Accepted in source	Proposed
007	Owned storage	Accepted in source	SQLite current; migration proposed
008	JWT/RBAC	Accepted in source	Proposed
009	Discovery	Proposed	Implemented locally
010	Resilience/health	Proposed	Implemented with open finding
011	Verification	Proposed	Implemented; overall FAIL retained

Changes reconcile UC-05 and ADR-004/005/006 around RabbitMQ and MongoDB; preserve SQLite as the prototype while ADR-007's PostgreSQL target remains; and expose ADR-008's implementation gap. No Gateway-to-Notification gRPC integration or Gmail delivery is claimed for the current scope.

Submission boundary

This report supplies revised design, full updated ADRs and three rendered diagrams. Editable Markdown, Mermaid sources, evidence and an export script remain in the repository. Original PDFs under docs/references are unchanged snapshots. The report does not certify production readiness and does not imply that a video has been recorded.

ADR-001 Frontend framework

Decision status: Accepted in the original proposal. **Implementation:** Proposed; no frontend application in this repository. **Revision:** 27 October 2026. **Origin:** original proposal pp. 13-14.

Context

Reporter, Central Admin and Department Staff need reusable reporting forms, ticket timelines and queues, with a mobile-friendly Thai interface.

Alternatives

React offers reusable components and TypeScript; Vue offers approachable components/reactivity; Angular supplies more built-in structure with greater setup and learning work.

Decision

Retain React with TypeScript as the target frontend. Define routing, form validation and shared API types when frontend work begins. The current deliverable exposes backend JSON APIs and terminal verification.

Consequences

UI consistency and shared types can reduce duplication. Routing, accessibility, responsive layout and browser support still require implementation and testing. A backend response benchmark is not a page-load or usability test.

Verification

NOT_RUN: Thai/mobile usability, supported browsers and the original public-page load target below 2 seconds. No UI completion is claimed.

ADR-002 Backend framework

Decision status: Accepted in the original proposal. **Implementation:** Implemented for Gateway, Ticket and Department. **Revision:** 27 October 2026. **Origin:** original proposal pp. 14-15.

Context

The team needs independently structured services with validation, dependency injection, REST and gRPC while keeping TypeScript across the stack.

Alternatives

Go offers compiled services but adds a language and learning cost. Express is minimal but leaves conventions to the team. NestJS supplies modules, injection and transport integrations with decorator/configuration overhead.

Decision

Retain Node.js, NestJS and TypeScript in separate applications. Share the versioned ticket proto contract and npm workspace tooling without sharing database access. RabbitMQ notification processing remains target work, and Gmail remains future work.

Consequences

Each service needs its own configuration, deployment, health and monitoring. Shared source/tooling does not remove service boundaries or operating costs.

Verification

PASS: current Docker builds compile all three applications and actual Gateway REST-to-REST/gRPC paths were tested. Auth/Notification applications are not implemented. See evidence run 20261027t084152z-c1ab.

ADR-003 Manual department routing

Decision status: Accepted in the original proposal. **Implementation:** Assignment/reassignment API implemented; authenticated admin UI is Proposed. **Revision:** 27 October 2026. **Origin:** original proposal pp. 15-16.

Context

Campus departments have overlapping responsibilities. Incorrect automated routing can bounce tickets between teams, so an administrator must review and choose a department.

Alternatives

Automatic classification may reduce dispatch work but requires evaluation and a correction workflow. Human review costs staff time and depends on administrator availability.

Decision

Retain human selection of the department. Ticket Service validates the department via REST and permits assignment from SUBMITTED or ASSIGNED. No AI routing or automatic spam classification is introduced.

Consequences

Human oversight supports correction and reassignment but does not guarantee routing accuracy or eliminate spam. RBAC must eventually protect assignment; currently the API does not enforce the conceptual actor role.

Verification

PASS: assignment and missing-department non-mutation in current evidence. Reassignment capability exists in source; NOT_RUN as a dedicated case in Person 3's latest suite. Admin permission enforcement is not implemented.

ADR-004 Asynchronous notification processing

Decision status: Accepted in the original proposal; contradictory delivery wording clarified. **Implementation:** Proposed; current Ticket Service has a notification log stub. **Revision:** 27 October 2026. **Origin:** original proposal p. 16 and UC-05 p. 6.

Context

Ticket updates should complete independently of notification processing. The original document selected RabbitMQ/MongoDB but retained stale Gmail postconditions and a synchronous notification route.

Alternatives

Portal polling needs repeated visits. A synchronous notification RPC couples ticket latency to the consumer. Direct email delivery requires credentials and provider failure handling. Asynchronous events separate these responsibilities but introduce delivery uncertainty.

Decision

The target is Ticket Service publishing AMQP events to RabbitMQ; Notification Service consumes and stores records in its own MongoDB. UC-05 succeeds when a notification record is stored and the message acknowledged. Gmail delivery is Future. Gateway does not orchestrate notification RPCs.

Consequences

Consumer failure must not roll back committed ticket changes. Publishing after commit can lose events on failure; logging alone is not reliable delivery. An outbox/publisher recovery design is future work before any guaranteed-delivery claim. Broker redelivery requires idempotent record creation.

Verification

NOT_RUN: broker publication, consumer delivery, MongoDB persistence or deduplication. Current logs prove only stub execution. UC-05 is not implemented by that stub.

ADR-005 Service communication boundaries

Decision status: Accepted in the original proposal; conflicting notification sentence removed. **Implementation:** REST/gRPC subset Implemented; other paths Proposed or Future. **Revision:** 27 October 2026. **Origin:** original proposal p. 17.

Context

Browsers need HTTP APIs; ticket workflows benefit from a proto contract; department lookup is synchronous; notification recording should be asynchronous.

Alternatives

REST everywhere simplifies tooling but changes the existing ticket contract. gRPC everywhere adds browser translation. Synchronous notification RPCs couple workflow completion to notification availability.

Decision

• Implemented: client tools to Gateway via local HTTP REST; Gateway to Ticket via gRPC; Gateway/Ticket to Department via REST.

• Proposed: browser to Gateway via REST/HTTPS; Gateway to Auth via REST and Cloudinary via HTTPS; Ticket to RabbitMQ via AMQP; RabbitMQ to Notification consumer via AMQP; Notification to MongoDB via its driver.

• Future: Notification to Gmail via HTTPS; Analytics API integration.

The Gateway-to-Notification gRPC path from the original text is removed. No cross-service database access is allowed.

Consequences

The team maintains HTTP DTOs, proto compatibility and a proposed event schema. Local HTTP/insecure gRPC is a development boundary, not proof of production transport security. Event publication is separate from ticket commit.

Verification

PASS: implemented paths, request IDs and DNS. NOT_RUN: HTTPS deployment, Auth, media uploads and AMQP/MongoDB integrations. Three revised diagrams use these same boundaries.

ADR-006 RabbitMQ broker

Decision status: Accepted in the original proposal. **Implementation:** Proposed; no broker or consumer is deployed. **Revision:** 27 October 2026. **Origin:** original proposal p. 18.

Context

Notification records should be processed independently of Ticket Service availability and support safe redelivery.

Alternatives

A direct synchronous call adds availability coupling. A stream platform adds operational scope beyond this iteration. RabbitMQ supports the queue/acknowledgement model selected in the original design.

Decision

Retain RabbitMQ for AMQP ticket notification events. The first target consumer stores MongoDB records using a unique eventId and acknowledges after successful storage. Suggested event fields are eventId, eventType, ticketId, recipient, occurredAt and schemaVersion; these are proposed contracts, not existing proto fields.

Consequences

Manual acknowledgements can allow redelivery after consumer failure, so consumers must deduplicate. Publisher confirms and consumer acknowledgements cover different sides of delivery [R6]. Neither alone makes the SQL commit and broker publication atomic. Durable configuration, publisher confirms and failure policy must be verified during integration. Application publisher retries/outbox are not implemented; no exactly-once guarantee is claimed.

Verification

NOT_RUN: broker restart, publish failure, redelivery, deduplication and backlog handling. Add these checks before claiming asynchronous notification reliability. [R6] is listed in the proposal references.

ADR-007 Service-owned data storage

Decision status: Accepted in the original proposal for the target design. **Implementation:** SQLite per service Implemented; PostgreSQL/MongoDB migration Proposed. **Revision:** 27 October 2026. **Origin:** original proposal p. 18.

Context

Auth, Ticket and Department require relational data. Notification records are event-oriented. The runnable prototype currently uses independent SQLite files rather than the target hosted databases.

Alternatives

A shared database allows accidental cross-service coupling. SQLite makes local setup simple but does not demonstrate multi-replica write scaling or hosted availability. Separate PostgreSQL databases retain ownership while requiring migrations and operations.

Decision

Retain PostgreSQL on Render as the original relational target, with a separate owned database/schema and credentials per Auth, Ticket and Department boundary. Retain MongoDB for Notification. Current Ticket/Department use TypeORM with better-sqlite3, separate /data paths and named volumes. Services collaborate through APIs/events, never another service's tables.

Consequences

Prototype persistence across container recreation is not backup/restore. A PostgreSQL migration needs explicit migrations, export/import, record/history reconciliation, staging tests, credentials, backup/restore checks and a rollback plan. Disable schema synchronization in a production migration plan. Render deployment feasibility and database operations remain unverified.

Verification

PASS: selected Department and ticket/history fixtures survive both container recreations in run 20261027t084152z-c1ab. NOT_RUN: PostgreSQL/MongoDB migration, backup recovery, HA and concurrent write capacity.

ADR-008 JWT authentication and RBAC

Decision status: Accepted in the original proposal. **Implementation:** Proposed; no Auth Service, JWT validation or RBAC guards. **Revision:** 27 October 2026. **Origin:** original proposal pp. 18-19.

Context

Registered users and guest reporters have different permissions. Central Admin routes tickets/manages departments; Department Staff handles its own queue; Reporters act on their own reports.

Alternatives

Server sessions require shared/session persistence across API instances. JWT supports explicit claims but needs signature, expiry, issuer/audience and lifecycle controls. Anonymous email fields alone do not establish identity.

Decision

Retain JWT for registered sessions, restricted guest credentials and RBAC plus ownership/department checks. The target Gateway authenticates incoming requests; services must enforce applicable resource permissions rather than trusting arbitrary reporterEmail/departmentId input. Detailed token lifecycle and guest ownership rules still require specification.

Consequences

Current APIs accept caller-supplied identities without guards, so the three actors describe requirements, not enforced permissions. Local benchmark traffic is unauthenticated. Authentication work will change latency and needs renewed measurements.

Verification

NOT_RUN: JWT signature/expiry, guest restrictions, Reporter ownership, Admin-only routing/CRUD and cross-department denial. Add positive and negative authorization tests before exposing the application as a user-facing service.

ADR-009 Service discovery

Decision status: Proposed; explicit team ratification pending. **Implementation:** Compose DNS implemented and verified locally. **Date:** 27 October 2026.

Context

Local npm development uses localhost endpoints. Container localhost refers to the caller itself, and replacement containers should remain reachable without editing every client URL.

Alternatives

Static container IPs require manual updates. Environment URLs configure an address but do not discover changing IPs. A dedicated registry adds deployment and client complexity. Platform DNS can provide stable logical names within its network.

Decision

Use Docker Compose service-name DNS on one backend bridge network for local/demo: ticket-service:50051 and http://department-service:3001. Publish only Gateway on host loopback, default port 3000; allow an isolated test port. Keep root .env localhost defaults for npm development. Clients reconnect after replacement; do not encode observed IPs [R3].

For a potential Render deployment, evaluate the provider's private service hostnames in the same region and eligible service types [R7]. Do not reuse Compose-only names on the host or cloud, or assume free services can receive private traffic. Cloud deployment remains Proposed.

Consequences

DNS, readiness and reconnection are distinct. Startup ordering uses service_healthy, but it is not runtime failover [R4]. A single host has no HA guarantee. Compose may reuse an IP; unchanged IPs do not invalidate stable-name discovery evidence.

Verification

PASS: names resolve inside Gateway, configured URLs match the contract, Department/Ticket container IDs change, Gateway ID stays constant, fixture reads succeed after readiness/reconnection, and data persists. See discovery.json in run 20261027t084152z-c1ab. NOT_RUN: multi-host discovery, load balancing or Render deployment.

ADR-010 Resilience and health

Decision status: Proposed; explicit team ratification pending. **Implementation:** Implemented with one open error-classification finding. **Date:** 27 October 2026.

Context

An unreachable or unresponsive dependency must not hold requests indefinitely or leave a failed pre-commit assignment partially saved. Liveness and dependency readiness serve different operational decisions.

Alternatives

Unbounded calls risk accumulating requests. Retry-all may duplicate mutations. A single health flag hides partial route availability. A circuit breaker could reduce repeated work but adds state and tuning beyond this prototype.

Decision

Use HTTP /health and /ready on Gateway/Department, and application-specific TicketService.CheckHealth with a database check. Bound REST calls including body reads to 2s; Gateway gRPC uses a native 3s deadline; Ticket's Department lookup is at most 2s and shortened to its remaining incoming deadline. Readiness checks use 750ms budgets. Propagate cancellation and check it before writes [R5].

Map UNAVAILABLE to HTTP 503 and DEADLINE_EXCEEDED to 504. Keep automatic mutation retries disabled. Save ticket and history in one local transaction; a Department failure before commit leaves both unchanged.

Consequences

Readiness 503 can coexist with working independent routes. Deadlines may expire after commit, leaving the client uncertain; reconcile before another mutation. The current Ticket health RPC is not grpc.health.v1. No circuit breaker, failover or idempotency scheme is implemented.

Verification

PASS: Department stopped/frozen, Ticket frozen, non-mutation, recovery and health probes. FAIL: stopped Ticket returned 504 in 3,027.05ms rather than the stronger smoke expectation 503, repeated twice. Existing code maps the observed deadline to 504; the transport cause remains open. Do not claim all stopped peers return 503. See findings.md; no target was relaxed.

ADR-011 NFR verification and observability

Decision status: Proposed; explicit team ratification pending. **Implementation:** Runner/evidence and request correlation implemented. **Date:** 27 October 2026.

Context

The original proposal includes query latency, availability, security and 1,000 active users, but local smoke checks cannot establish all of them. Claims need a declared workload, provenance and limitations.

Alternatives

Single manual requests lack repeatability. A production load suite offers broader evidence but requires deployment, identity and resource isolation. A bounded local runner provides a reproducible progress baseline without pretending to prove production capacity.

Decision

Use node scripts/verification/run.mjs on fresh isolated Compose projects. Benchmark GET /tickets and history separately with 100 tickets, 10s warm-up, 20 closed-loop workers and 60s measurement each. Provisionally require p95 below 1s and error below 1%; retain the original requirements rather than redefining them. Record all attempts, nearest-rank percentiles, drain-inclusive throughput, environment, commit/dirty flag, source hashes and raw CSV. Audit calculations independently.

Propagate/echo validated x-request-id across HTTP and gRPC. Capture structured service logs for correlation; this is not full distributed tracing. Distinguish PASS, FAIL and NOT_RUN; keep previous failed runs.

Consequences

Host load generation and shared Docker resources constrain inference. Closed-loop traffic reduces its arrival rate when responses slow down. Passing p95 does not prove all responses below 1s, 1,000 active users or 99.5% uptime. New authentication/database/infrastructure work requires new measurements.

Verification

PASS: both provisional performance criteria, raw CSV audit, workflow/filters, correlation, discovery/persistence and restoration. Overall FAIL remains due to stopped-Ticket status classification. NOT_RUN: production capacity, soak/uptime, concurrent writes, security and cloud/HA validation. Use run 20261027t084152z-c1ab and preserve its open finding.

15 References and evidence

Requirements snapshots

• [R1] Project description and ADRs, 19 pages. Actors/problem p. 1; UC-01 to UC-08 pp. 2-9; functional requirements pp. 10-12; NFRs pp. 12-13; ADR-001 to ADR-008 pp. 13-19. Original accepted decisions and team roster retained; inconsistent notification wording revised in this report.

• [R2] Microservice architecture, 2 pages. Original architecture and service operation catalog. The revised views explicitly label implementation status rather than treating all drawn components as deployed.

Primary technical references

• [R3] Docker Compose networking: logical service names, network scope and replacement connections.

• [R4] Docker Compose startup order: depends_on and service_healthy startup behavior.

• [R5] gRPC deadlines and cancellation: bounded calls and application cancellation handling.

• [R6] RabbitMQ consumer acknowledgements and publisher confirms: separate consumer/publisher responsibilities and redelivery considerations.

• [R7] Render private network: provider internal hostnames and service eligibility; deployment not verified here.

Technical references checked 27 October 2026. Implementation claims primarily use repository source and the evidence below, not provider documentation as proof of this deployment.

Reproducible project evidence

• [E1] Latest report, with summary.json, environment.json, fixtures.json, raw CSV, audit.json, discovery.json, functional.json, failure.json, request-correlation.json and final-containers.jsonl in the same directory. Run command: `node scripts/verification/run.mjs`. **Overall FAIL** remains recorded.

• [E2] Stopped-Ticket finding and earlier retained run.

• [E3] NFR verification guide, discovery guide, resilience guide, and handoffs 1, 2, 3. Local commands and current health/API contracts are recorded there.

• [E4] Implementation: compose.yaml; proto/ticket.proto; services/api-gateway/src, services/ticket-service/src and services/department-service/src; scripts/verification. Source/config hashes accompany the benchmark because the working tree was uncommitted.

Editable deliverables

Proposal source: docs/proposal.md. Full decisions: docs/adr. Figure sources/renders: docs/diagrams. PDF/export tooling: docs/build. Final consolidated artifact: docs/proposal.pdf. The PDF embeds the full ADR sources when rebuilt; Markdown readers can open each linked record above.
